

CREMS Mid Term Review Report

Car and Rental Equipment Management System

Carpenters Fiji Pte Limited

CS400 Industry Experience Project

Semester 2 2026

Group 10

Team member	Student ID
Kavish Chandra	S11219143
Sudhansu Jayshil Kisun	S11219520
Shoneel Kumar	S11219651
Rahul Chand	S11219885

Academic supervisor Dr Ravneil Nand

Report date 16 September 2026

Planned project completion 30 October 2026

Prepared for academic and client review

Executive Summary

We are developing CREMS for Carpenters Motors and Carptrac to bring customer requests, asset records, quotations, approvals and hire operations into one system. During the first half of the project, we established the application and database, implemented the main customer and staff interfaces, and began integrating the full rental workflow.

Our current build supports customer and staff access, branch-based permissions, booking workspaces, configurable approvals and guided pickup and return. Recent testing identified problems with inspection uploads, saving inspection records, session expiry and catalogue images. We corrected these problems and added targeted checks to reduce the chance of recurrence.

Our next priority is to complete and test the vehicle and equipment hire journeys from booking through return. Maintenance, equipment-specific requirements, reporting and client acceptance testing remain in the delivery plan. We are working towards the planned completion date of 30 October 2026.

Contents

Section	Page
1 Project context and scope	3
2 Functional requirements	4
3 Quality and ethical requirements	5
4 System architecture and data model	6
5 User responsibilities and workflow design	7
6 Milestones and engineering evidence	8
7 Plan changes and issues resolved	9
8 Risk management update	10
9 Remaining delivery plan	11
10 Teamwork and project control	12
11 Conclusion and references	13

1 Project Context and Scope

Business problem

Carpenters Fiji manages rental vehicles and equipment with different operating rules. Vehicle hire involves licence eligibility, fuel and odometer readings. Equipment may require capacity checks, operators, transport, engine-hour tracking and additional approval. Separate operational records make it harder to establish availability, reconstruct condition at handover and relate asset income to maintenance costs.

CREMS provides a shared record across the hire lifecycle. A booking connects the customer, branch, asset and hire period. Inspections and agreements remain associated with that booking, while the asset register provides the longer-term asset history. A general asset inspection therefore does not establish the condition of a particular customer hire.

Objectives

Our objectives are to provide secure access, accurate availability and booking records, configurable pricing and approval, reliable inspection evidence and useful operational reports. We will assess these objectives through complete user tasks, including checking that records are saved and accessible only to authorized users.

Included in the delivery scope	Outside the MVP or separately controlled
Motors vehicles and Carptrac equipment; configurable branches, categories and attributes.	Additional divisions require operational validation and their own acceptance work.
Customers, assets, availability, quotes, bookings, approvals and hire documents.	Full accounting/ERP replacement, payroll and banking reconciliation.
Inspection evidence, handover, return, maintenance and expenditure.	Live telematics, advanced route optimization and native offline applications.
Operational reports, audit, notifications and profitability measures.	Production payment gateway, third-party identity and large historical migration unless approved.

Stakeholders and expected value

Customers need clear charges and booking status. Rental officers need reliable queues; managers need scoped oversight and approval evidence. Maintenance staff need service and condition history. Client sponsor Amit Kumar and academic supervisor Dr Ravneil Nand provide business and academic review.

We expect the system to reduce duplicate records, clarify responsibility during handover and improve visibility of asset use and maintenance costs. We will evaluate these benefits through client testing once the complete workflow is ready.

2 Functional Requirements

We have grouped the main requirements below to show what is implemented and what still needs verification. Final acceptance will depend on completing the relevant user scenario, checking the saved records and confirming access restrictions.

ID and requirement	Current position	Required acceptance evidence
FR01 Identity and access	Implemented; wider security verification remains.	Customer sees own records only; staff role and branch restrictions hold at API level.
FR02 Customer records	Portal and staff administration demonstrable.	Create and update customer; retrieve permitted documents and reject unauthorized access.
FR03 Assets and catalogue	Implemented; image recovery verified locally.	Persist attributes, branch and status; display catalogue photos correctly.
FR04 Availability and requests	Booking and quote flows implemented and refining.	Reject unavailable hire; retain dates, branch and request reference.
FR05 Pricing and quotations	Pricing workspace and quote decisions implemented.	Charges, tax, deposit and revisions match agreed examples.
FR06 Configurable approvals	Ordered stages and scoped decisions implemented.	Triggered hire completes required stages before confirmation.
FR07 Pre-hire and checkout	Guided flow and independent saving implemented; targeted tests pass.	Save and reopen photos/checklist without checkout; complete handover separately.
FR08 Return and post-hire	Return and comparison implemented; browser payload checks completed.	Retain evidence; apply correct asset status and damage referral.
FR09 Maintenance and costs	Foundation exists; operational completion remains.	Record job costs and downtime; verify return-to-service control.
FR10 Reports and notifications	Partial; reconciliation and delivery verification remain.	Reconcile reports to transactions; verify delivery outcome and audit history.

Traceability and change control

For the remaining tests, we will record the requirement, test data, expected outcome and actual result. Where a client rule changes, we will update the requirement and its test together.

3 Quality and Ethical Requirements

Quality targets

Our quality targets are two seconds for routine interactions and five seconds for longer operations, with at least 80 percent unaided completion of core tasks during usability testing. We will measure these targets during integration testing and client user acceptance testing.

Area	Required control and verification
Access and sessions	Enforce role and branch scope on the server. Test expiry, active renewal, logout and prohibited access using separate accounts.
Integrity	Validate dates, meters, payments and lifecycle transitions. Verify persistence after reload and conflicting operations.
Files and privacy	Restrict photo types and sizes; protect private documents and signatures. Verify download authorization and agree retention rules.
Recovery	Maintain migrations and recoverable configuration. Rehearse backup restoration and clean setup before handover.
Usability	Use labelled controls, clear errors and consistent navigation. Verify keyboard access, responsive layouts and representative tasks.

Handling personal information and condition evidence

The system handles identity documents, photographs and signatures, so we need to limit collection and access to what is necessary for a hire. Inspection images should focus on the asset and avoid unrelated personal information. OWASP recommends validating file types, limiting upload size and checking upload permissions [1]. We have added image validation and size controls; retention and private-access checks remain part of our security review.

Inspection records may be used when reviewing damage and charges. We therefore keep the evidence linked to the booking and responsible staff member. A saved pre-hire inspection is separate from final handover, and a recorded damage concern must still be reviewed before a charge is confirmed.

Transparency and professional responsibility

We need to present rental charges, additional services and refundable bonds clearly so customers understand the quotation. Staff access must reflect their responsibilities, and approval decisions must remain traceable. We will use non-sensitive demonstration data and follow the client's confidentiality requirements when sharing project material.

4 System Architecture and Data Model

The web application uses React 19, TypeScript, Vite and Material UI. An ASP.NET Core API on .NET 10 applies business rules, and Entity Framework Core persists records in SQL Server. The development database runs in Docker.

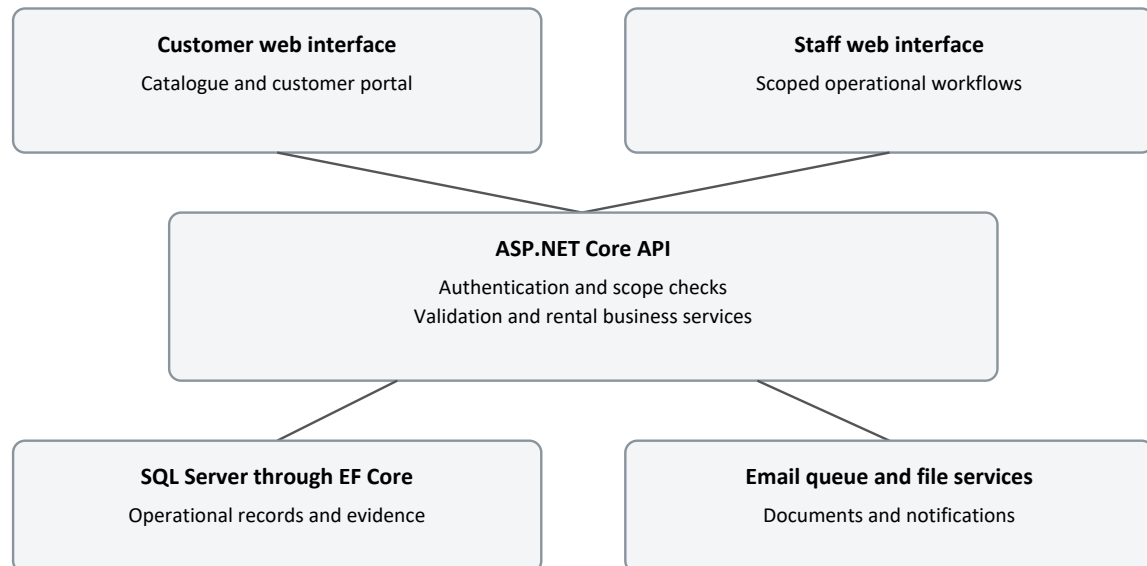


Figure 1 Logical architecture of the development system

Our API checks the user, permitted scope and business state before making protected changes. This follows the distinction between establishing a user's identity and deciding what that user may access in ASP.NET Core authorization [2]. Browser checks provide immediate feedback, while the server enforces the rules.

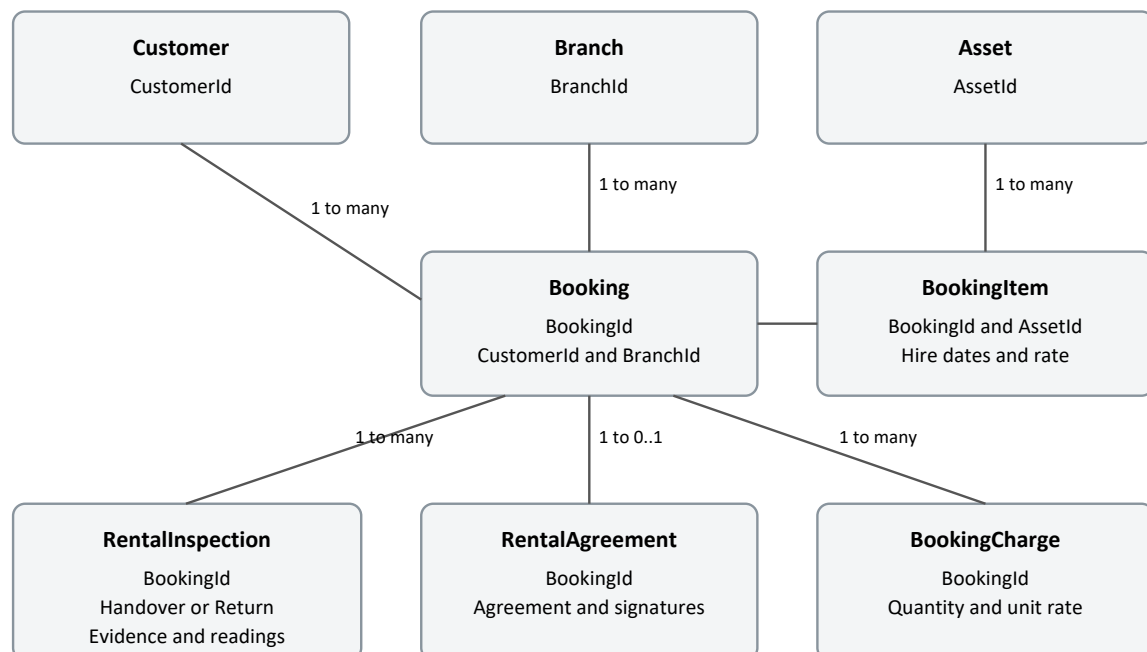


Figure 2 Selected rental entities and relationships

BookingItem connects each asset and hire period to a booking. RentalInspection stores handover and return evidence. A booking can have several items. The diagram shows the main rental relationships; approval, payment and user-access entities support these records.

5 User Responsibilities and Workflow Design

Actor	Principal use cases
Visitor and Customer	Browse rentals; request booking or quotation; manage own profile and monitor own requests and documents.
Rental Officer	Review requests, prepare pricing, allocate assets and perform authorized pickup, inspection and return.
Branch Manager	Review branch activity and decide assigned approval stages within permitted scope.
Maintenance Officer	Review asset condition and carry out authorized maintenance and service updates.
Administrator and Super Administrator	Manage permitted accounts and configuration; reserve system-wide governance for appropriate authority.

We removed separate Driver or Operator and Finance Officer login roles from the current scope. Driver and operator requirements remain part of rental planning and charges. This keeps the login model focused on the users who need to operate the system.

Pickup and inspection sequence

A confirmed booking opens the existing Pickups & returns workflow from Bookings & quotations. Staff confirm the customer, scan the asset, verify documents, record meter and fuel, complete the pre-hire inspection, review the agreement, obtain the customer signature and perform agent checkout. Authorized operational staff conduct the inspection.

The pre-hire step saves a preparation record independently. Reopening should restore checklist, photos and readings. Saving must not change the booking into an active hire; checkout is a separate action with its own readiness checks. General Asset register inspections remain asset records. Rental pre-hire and post-hire evidence belongs to the booking workflow.

Return and equipment variations

At return, staff record condition and readings, compare pre-hire evidence and record damage and accessories. The next asset state depends on the result and maintenance needs. Vehicle-specific licence and meter fields must not block equipment where they do not apply. Equipment acceptance also requires appropriate operator, engine-hour and safety scenarios.

Project-specific design contribution

We designed the shared workflow around configurable asset categories, inspection templates and approval stages. This lets us accommodate vehicle and equipment differences without maintaining separate versions of the same process. Booking and QR entry points open the existing operational workflow, which also makes navigation more consistent.

6 Milestones and Engineering Evidence

Our project schedule runs from 10 August to 30 October 2026. We are in Week 6 at this review. Some approval and rental functions have been developed earlier than planned, allowing us to identify integration problems before the scheduled lifecycle demonstrations.

Baseline milestone	Position at review
M1 Week 1 Scope and foundation	Plan, repository, API, web application and database available. Approval records remain part of project governance.
M2 Week 2 Secure sign-in	Authentication and sessions implemented; active-session renewal corrected during testing.
M3 Week 3 Access isolation	Role and branch scope implemented; full isolation regression remains required.
M4 Week 5 Asset register	Asset/category interfaces and catalogue available; targeted image checks completed.
M5 Week 7 Quotation to booking	Booking and staged approvals implemented; complete notification and agreement demonstration remains.
M6 Week 8 Motors lifecycle	Guided pickup/return implemented early; targeted defects corrected and tests added.
M7 Week 10 Carptrac lifecycle	Equipment foundation available; personnel and engine-hour acceptance remains.
M8 Week 12 Handover	Deployment, final acceptance, guides and closure remain planned.

Completed development verification

Our latest backend test run passed all 31 tests. We also checked that an inspection could be inserted with photo and checklist evidence, retrieved after clearing the database context, and updated without changing the booking status. We rolled back the test transaction after verification.

We tested photo selection, resizing, invalid-file errors, previews and the pickup and return forms. These component tests used mocked API writes, so full authenticated workflow tests remain necessary. We also checked all 32 restored catalogue image URLs and confirmed that 12 visible photos loaded in headless Chrome.

7 Plan Changes and Issues Resolved

Changes from the baseline

We brought configurable approvals and parts of the hire workflow forward because they affect booking confirmation and asset handover. This helped us find integration problems early. We also simplified customer handling and removed unnecessary login roles to keep the initial scope manageable. Our remaining schedule keeps time for testing and handover rather than adding further optional features.

Observed issue	Engineering response	Verification and remaining work
Inspection could not save	Register new inspections explicitly for insertion; reuse the preparation record on subsequent saves.	Regression tests and rolled-back SQL insert/read/update passed; user workflow retest remains.
Photo attachment unreliable	Shared picker with decoding, resizing, limits, previews and processing status.	Browser checks cover valid and corrupt files; real device and camera checks remain.
Save could lead to login	Renew server session during active use while retaining inactivity expiry.	Controlled-clock tests cover active/idle behaviour; full session regression remains.
Catalogue images broken	Restore missing bundled seed images and avoid stale failed-image cache responses.	32 URLs passed; 12 visible photos decoded.
Booking inspection entry confusing	Redirect to existing Pickups & returns with the selected booking.	Focused booking and preparation checks added; no separate inspection page needed.
Equipment pickup had vehicle assumptions	Allow non-applicable driver/meter fields while retaining applicable readiness checks.	Targeted request and workflow tests; full equipment acceptance remains.

Lessons and unresolved work

These issues showed us that checking a form on screen is not enough. We now check whether its data survives a reload and whether errors are handled clearly. We still need to complete broader integration tests and resolve remaining administration issues before the release.

8 Risk Management Update

We review risks using probability and impact scores from 1 to 5. The table retains our baseline ratings and shows the actions taken or still required. New technical risks from inspection saving, session expiry and media handling are described below.

Risk and baseline score	Mitigation and current position	Accountable role
Scope/capacity R1/R3 20 High	Maintain initial division boundary; defer optional scope before reducing verification time.	Project Leader
Client availability R2 16 High	Book focused reviews early; log assumptions and request explicit operational decisions.	Project Leader
Scope leakage R4 15 High	Scoped queries and API policies exist; cross-branch negative tests remain necessary.	Backend lead
Invalid booking state R5 15 High	Validate transitions and persistence; test concurrency and duplicate submission.	Backend lead
Pricing R6 15 High	Reconcile decimal calculations and line items against client-approved examples.	Backend lead
Photo privacy R7 12 Medium	Type/size controls implemented; review private access, retention and storage growth.	Quality lead
Late mismatch R12 15 High	Demonstrate complete journeys; block handover on unresolved critical defects.	Project team
Test backlog R21 12 Medium	Targeted tests added; extend integration coverage before optional features.	Quality lead

Additional risks identified

The inspection fault showed that similar save operations could fail if new related records are not inserted correctly. Long forms also create a risk of session expiry, while missing image files can make the catalogue unusable. We will extend persistence tests, test realistic form durations and verify media files during deployment checks. The backend and quality leads will review these risks at the next checkpoint.

9 Remaining Delivery Plan

We have retained the original completion date and the planned maintenance, equipment and handover milestones. The remaining work focuses on completing the operational journeys, resolving defects and preparing for client testing.

Period	Deliverable and lead	Exit evidence
16–18 Sep	Stabilize rates, quotes and inspection saving. Backend and Quality leads.	Record survives reload; pricing matches examples; defects triaged.
21–25 Sep	Quotation-to-booking, approvals, agreements and notifications. Project and Backend leads.	Standard and triggered requests complete with correct references, documents and delivery outcome.
28 Sep–2 Oct	Motors lifecycle validation. Frontend and Quality leads.	Booking completes pre-hire, QR handover, return and post-hire with correct evidence and state.
5–9 Oct	Maintenance, damage and expenditure. Backend lead.	Job costs, downtime, referral and return-to-service restrictions verified.
12–16 Oct	Carptrac variations and UAT preparation. Backend and Frontend leads.	Operator, engine-hour, transport and safety cases pass; UAT scripts ready.
19–23 Oct	Reports and integrated UAT. Quality lead and client reviewers.	Reports reconcile; critical journeys pass; feedback corrected or formally deferred.
26–30 Oct	Stabilization and handover. Project Leader and all members.	Blocking defects resolved; restore/setup proven; guides, release and final assessment materials delivered.

Critical dependencies

Our reports depend on accurate rental and expenditure records, and return-to-service depends on inspection and maintenance outcomes. We will finish and test these transactions before validating the dashboards. If a delay affects this sequence, we will review scope and escalate the impact to the client.

Release criteria

Before handover, we will require critical business-rule and API tests to pass, agreed browser journeys to work, and significant security issues to be resolved or formally addressed. We will also complete client feedback review, performance checks and a backup restoration exercise.

10 Teamwork and Project Control

Responsibility baseline

We have divided the main responsibilities as follows. These roles give each work area a clear owner, while testing, documentation and presentation preparation remain shared tasks.

Member	Primary responsibility
Kavish Chandra	Project Leader/client liaison: scope, decisions, coordination, integration and submission.
Shoneel Kumar	Backend/data lead: API and domain model, database, migrations and authorization.
Sudhansu Jayshil Kisun	Frontend/UX lead: journeys, interface integration, accessibility and UI verification.
Rahul Chand	Quality/DevOps lead: tests, builds, environments, release, backup and documentation.

Communication and participation

Our communication plan uses weekly reviews to connect client feedback with requirements and the next development increment. This is consistent with the Scrum Guide's approach of reviewing outcomes with stakeholders and adapting subsequent work [3]. We will keep the remaining reviews focused on complete rental scenarios and decisions that affect delivery.

We have prepared requirements, technical models and workflow explanations to communicate the project to both technical and non-technical reviewers. For the next demonstrations, each member will explain the work in their area and help test the related parts of the system.

Change and knowledge control

We will record the reason and schedule impact of any material change before adding it to the remaining work. We use the repository to retain implementation history and will keep setup guidance and technical decisions available to all members. This is especially important for the security, pricing and inspection logic.

11 Conclusion and References

We have completed the main application foundation and implemented the customer, asset, booking and approval interfaces. We have also made progress on pickup and return, including correcting the inspection and image problems identified during testing. The project is now moving from individual feature development towards complete workflow verification.

Our focus for the second half is to complete the Motors and Carptrac hire journeys, finish maintenance and reporting, and work through client acceptance testing. We will keep optional changes under control so that testing, documentation and handover can be completed by 30 October 2026.

References

- [1] OWASP Foundation. *File Upload Cheat Sheet*. OWASP Cheat Sheet Series. Available online: https://cheatsheetseries.owasp.org/cheatsheets/File_Upload_Cheat_Sheet.html. Accessed 16 September 2026.
- [2] Microsoft. *Introduction to authorization in ASP.NET Core*. Microsoft Learn. Available online: <https://learn.microsoft.com/en-us/aspnet/core/security/authorization/introduction?view=aspnetcore-10.0>. Accessed 16 September 2026.
- [3] K. Schwaber and J. Sutherland. *The Scrum Guide*. November 2020. Available online: <https://scrumguides.org/scrum-guide.html>. Accessed 16 September 2026.
